Alameda Hospital 2030 Seismic Upgrades (February 2026 Update BOD)

print: Thu 2/26/26 (12:06 PM)
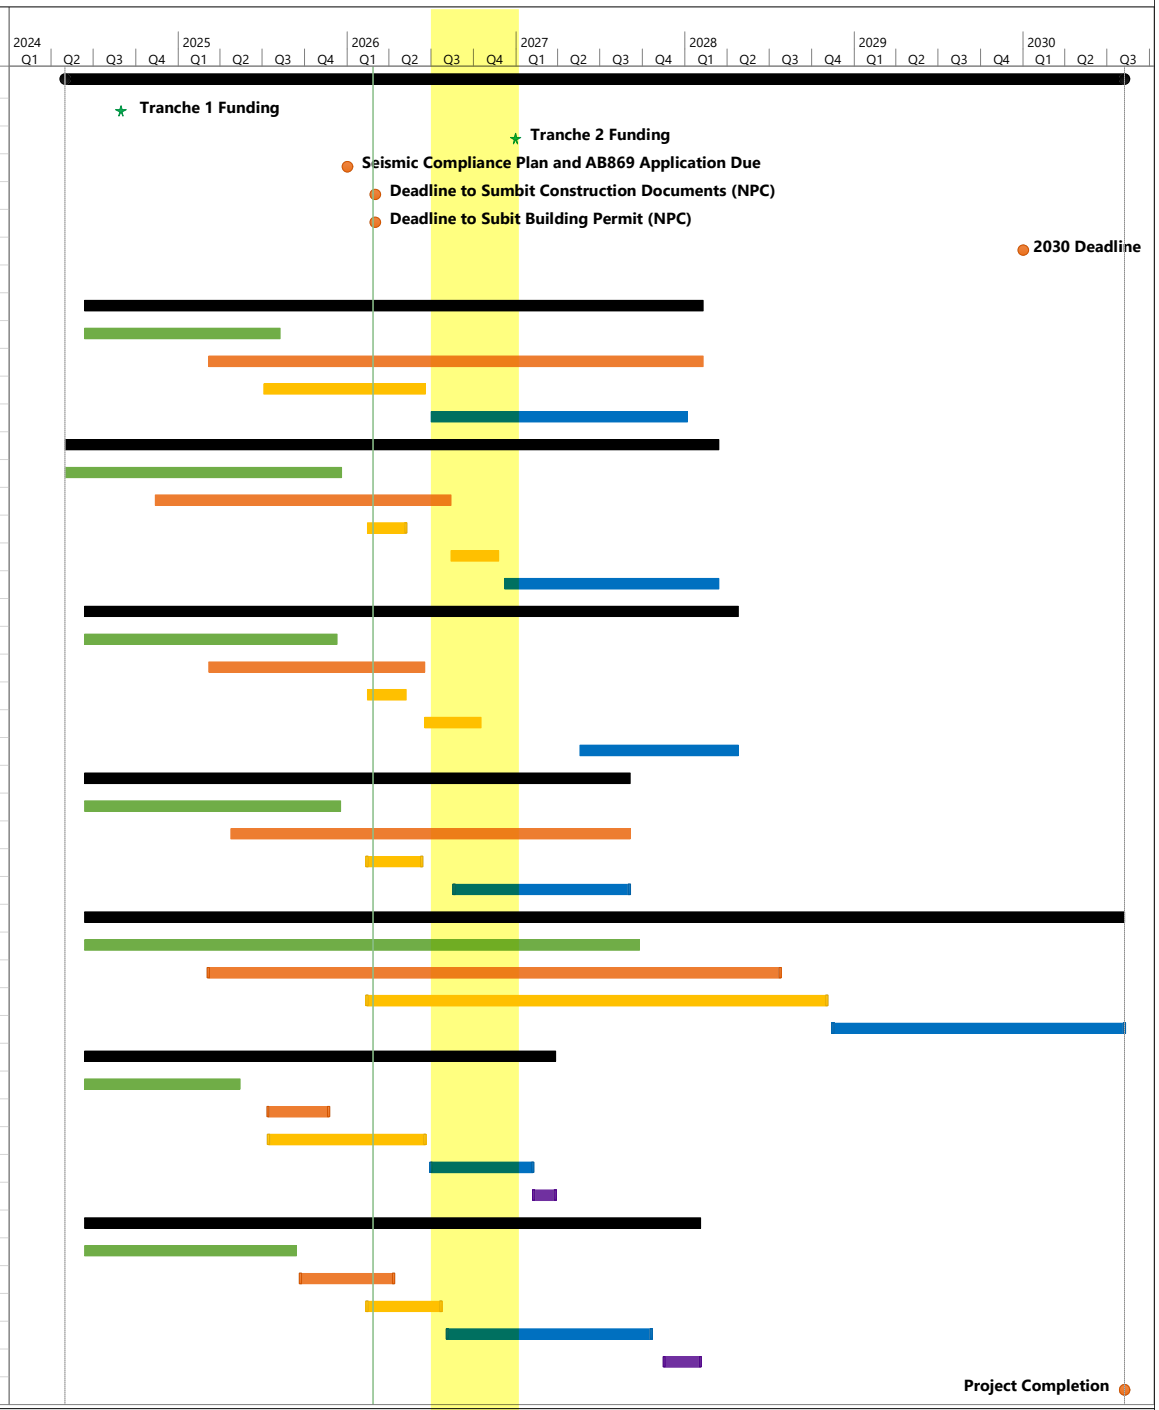
ID	Task Name
1	**ALAMEDA HOSPITAL**
2	Tranche 1 Funding
3	Tranche 2 Funding
4	Seismic Compliance Plan and AB869 Application Due
5	Deadline to Sumbit Construction Documents (NPC)
6	Deadline to Subit Building Permit (NPC)
7	2030 Deadline
8	
9	**MOMENT FRAME**
10	**Moment Frame Design - Structural Program**
19	**Moment Frame - Structural Program + Plan Permitting**
37	**Moment Frame Bid / Contract / Owner Procurement**
50	**Moment Frame Construction Milestones**
73	**NPC 4 - MEP and EQUIPMENT**
74	**NPC 4 Design**
86	**NPC 4 Permitting**
96	**NPC 4 Bid / Contract / Owner Procurement**
105	**NPC 4 Alternate Review / Execution**
110	**NPC 4 Construction Milestones**
126	**NPC 5 - TANKS**
127	**NPC 5 Design**
139	**NPC 5 Permitting**
157	**NPC 5 Bid / Contract / Owner Procurement**
166	**NPC 5 Alternate Review / Execution**
172	**NPC 5 Construction Milestones**
190	**SPC MATERIAL TESTING**
191	**SPC Material Testing Design**
199	**SPC Material Testing Program + Plan Permitting**
214	**SPC Material Testing Bid / Contract / Owner Procurement**
226	**SPC Material Testing Construction Milestones**
247	**SPC 4D**
248	**SPC 4D Design**
262	**SPC 4D Permitting**
280	**SPC 4D Bid / Contract / Owner Procurement**
294	**SPC 4D Construction Milestones**
309	**SNF MAKE READY**
310	**SNF Make Ready Design**
322	**SNF Make Ready Permitting**
329	**SNF Make Ready Bid / Contract / Owner Procurement**
342	**SNF Make Ready Construction Milestones**
354	**SNF Make Ready Licensing**
361	**SNF - SKILLED NURSING FACILITY**
362	**SNF Design**
373	**SNF Permitting**
380	**SNF Bid / Contract / Owner Procurement**
394	**SNF Construction Milestones**
409	**SNF Licensing**
416	***Project Completion***
